SRI BAALAMURUGAN BOREWELLS

4, gangamma Compound, Opp. Canara Bank Bus Stop, Bellary Main Road, Helbal Bangalore - 24
Mob : 9845020536, 9901920004

(1)

WORK REPORT

No.

Date :

Kogilu layout 6th cross.

S.No.	Particulars	Rft :	Water Yield	Remarks
1.	Size of The Borewell	165 mm		
2.	Total Deapth of The Borewell	984'		
3.	MS Casing Erected	196'		
4.	1st Water Source at the Deapth	300'		
5.	2nd Water Source at the Deapth	520'		
6.	3rd Water Source at the Deapth	700'		
7.	4th Water Source at the Deapth	950'		
8.	If any Silt, Boulders at the Deapth	-		
9.	Nature of Water	Sweet Water		
10.	Moter Pump to be Used	15 HP 25 Stage		
11.	Any other Remarks	-		
12.	Total Yield of the Borewell	2'.0"		

Thanking You

Yours faithfully
For Sri Baalamurugan Borewells

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE Byatarayanapura Sub Division

b) Location of the Site : BBMP Ward No-5

c) Area of the land : Kogilu layout 6th Cross Near Anganawadi

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA :

2) Recommended Site for drilling :

3) Total depth to be drilled : 800' to 1100'

4) Approx. casing pipe required : 110 to 150'

5) No. of water bearing Zones : —1—

6) No. of favourable spots marked : —1—

7) Qty. of water expected : 2½" to 3.0"

8) Method of survey carried out : GEO

9) Remarks :

P.T.O. : Terms & Conditions

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

BOREWELL SITE PLAN

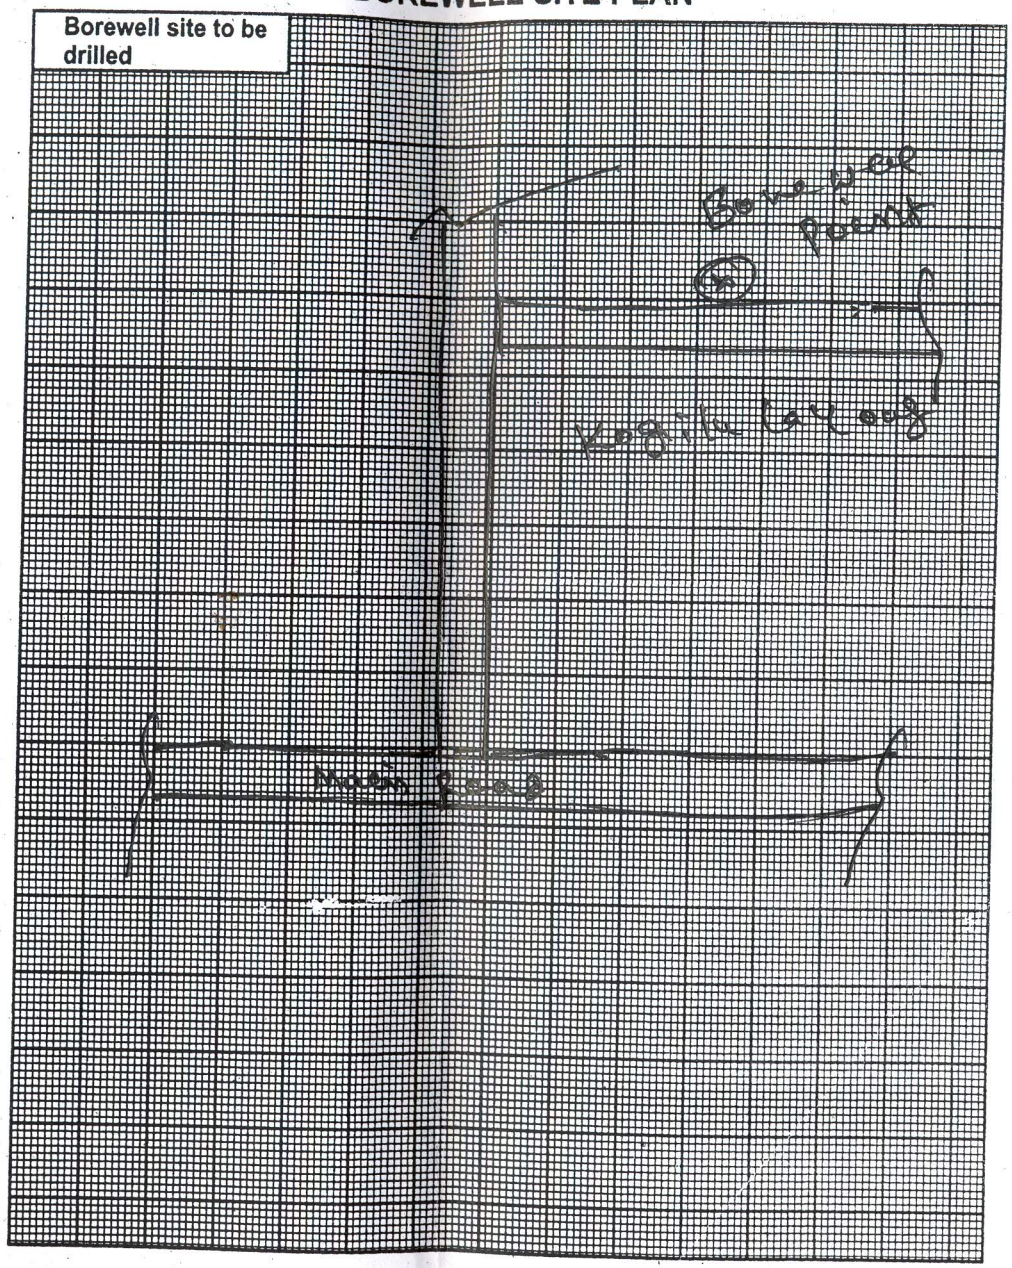

Name of work :- Drilling of borewell & providing hand pump at Sri Kogilu layout Kogilu Agrahara layout Agrahara Ward No-5 Byatarayapura Sub-division

Wd. No. 5 ಕೆಂಗಲಿಲು ಲೇಔಟ್ ನಲ್ಲಿ ಅಂತರ್ಜಲ ಅಂವೇಷಣೆ ಮತ್ತು ಕೈಪಂಪ್ ಅಳವಡಿಕೆ.

(1)

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

Assistant Executive Engineer
Byatarayanapura Sub Division
B.B.M.P. Bangalore

W.O. No 5 ಕೆಳಗಿನಲು ಆಳಿಕೆ ಅಂದಾಜುಪಟ್ಟಿ, ಬೆಂಗಳೂರಿನಲ್ಲಿ

(1)

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

Assistant Executive Engineer
Byatarayanapura Sub Division
B.B.M.P. Bangalore
